



Delivery Lot Summary Report: Pilot Delivery Lot 6 March 17, 2016

USGS Contract: G10PC00026


USGS Task Order: G15PD00640

Task Order Name: FEMA HQ – Shawano, WI QL2 LiDAR

Contractor: GMR Aerial Surveys, dba Photo Science, A Quantum Spatial Company

The following is a summary description of the deliverables and other pertinent information that comprise the shipment of Delivery Lot 6 to USGS on March 17, 2016.

Shawano County, WI Pilot Delivery Lot 6 Map:

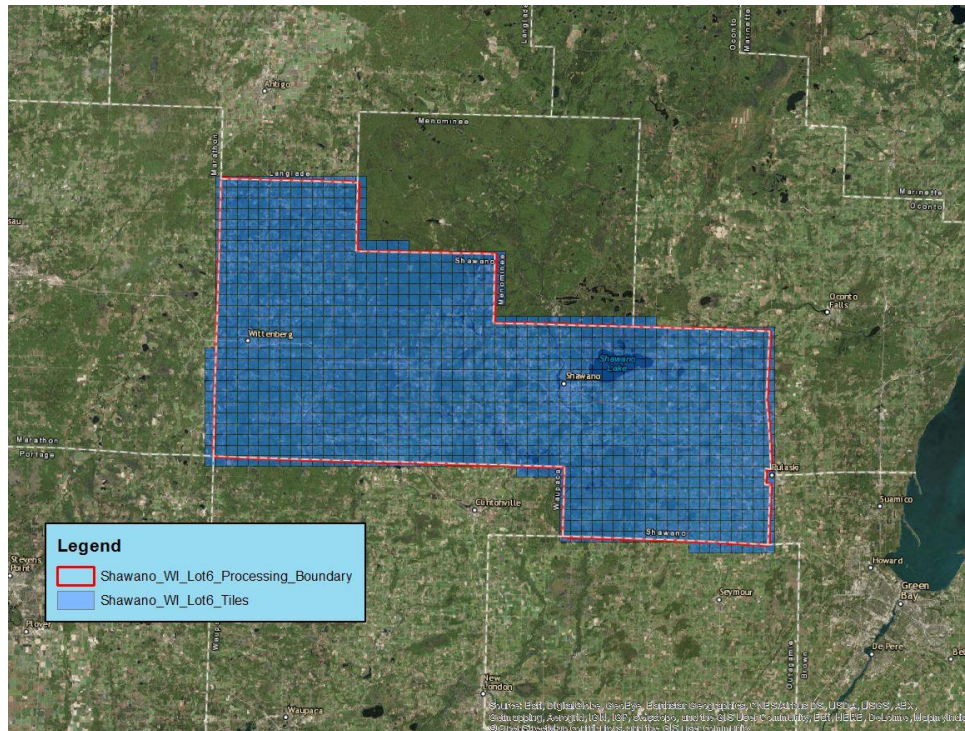

Task Order Spatial Reference System:

- Horizontal: UTM 16N, NAD83 (2011), Meters
- Vertical: NAVD88, GEOID12B, Meters



Deliverables Summary:

1. C.1.d.(i) Raw Point Cloud Data: Included
 - LAS v1.4, Point Record Format 6 including File Source ID
 - Classification Schema:
 - (00) Code 0 – Created, never classified
 - Total Number of Files: 73
 - Total File Size: 430 GB
2. C.1.d.(ii) Classified Point Cloud: Included
 - LAS v1.4, Point Record Format 6 including File Source ID w/assigned value of 0
 - Classification Schema:
 - (01) Code 1 – Processed, but unclassified
 - (02) Code 2 – Bare-earth ground
 - (03) Code 7 – Noise
 - (05) Code 9 – Water
 - (06) Code 10 – Ignored Ground (Breakline Proximity)
 - (07) Code 17 – Bridge Decks
 - (08) Code 18 – High Noise
 - Total Number of Tiles: 1,143
 - Tile Dimensions: 1,500m x 1,500m
 - Total File Size: 403 GB
 - Delivery Lot 6 Tile Shape Files (Lot 6 Individual Tiles)
3. C.1.d.(iii) Bare Earth Surface (Raster DEM): Included
 - Format: ERDAS .IMG
 - Resolution: 1 meter grid cell size
 - Hydro Conditioning: Hydro Flattened
 - Total Number of Tiles: 1,143
 - Tile Dimensions: 1,500m x 1,500m (same used for Classified Point Cloud)
 - Total File Size: 10 GB
4. C.1.d.(vi) Intensity Image
 - Format: GeoTIFF, with world files
 - Resolution: 1 meter pixel size
 - Scale: 8 bit, 256 color gray scale
 - Total Number of Tiles: 1,134
 - Tile Dimensions: 1,500m x 1,500m (same used for Classified Point Cloud)
 - Total File Size: 3.42 GB
5. C.1.d.(viii) Breaklines: Included
 - Format: ESRI Geodatabase Format
 - Coverage: Lot 6 Continuous, Non-Tiled
 - Total File Size: 1.86 MB



6. C.1.d.(ix) Metadata: Included
 - Format: FGDC compliant, XML
 - File Types: Project, Deliverable product group (Classified .las, DEM, Breaklines & Intensity Images)

7. C.1.d.(x) Project Report:
 - Delivery Lot Summary Report: Lot 6 Included
 - Overall Project Report: Lot 6 included.

8. Lot 6 QA & Accuracy Reporting
 - NVA QC Checkpoints FVA Testing Results (Excel File): Included
 - Calibration Control Point Testing Results (Excel File): Included
 - LAS Analysis (Excel File): Included
 - LAS Stats (Excel File): Included
 - DEM Stats (Excel File): Included

Delivery Lot Notes/Comments:

Delivery Lot 6 consists of all required deliverables for delivery lot 6.
